


## Re-Roof Project: Weekly Update

Tuesday, 18 October

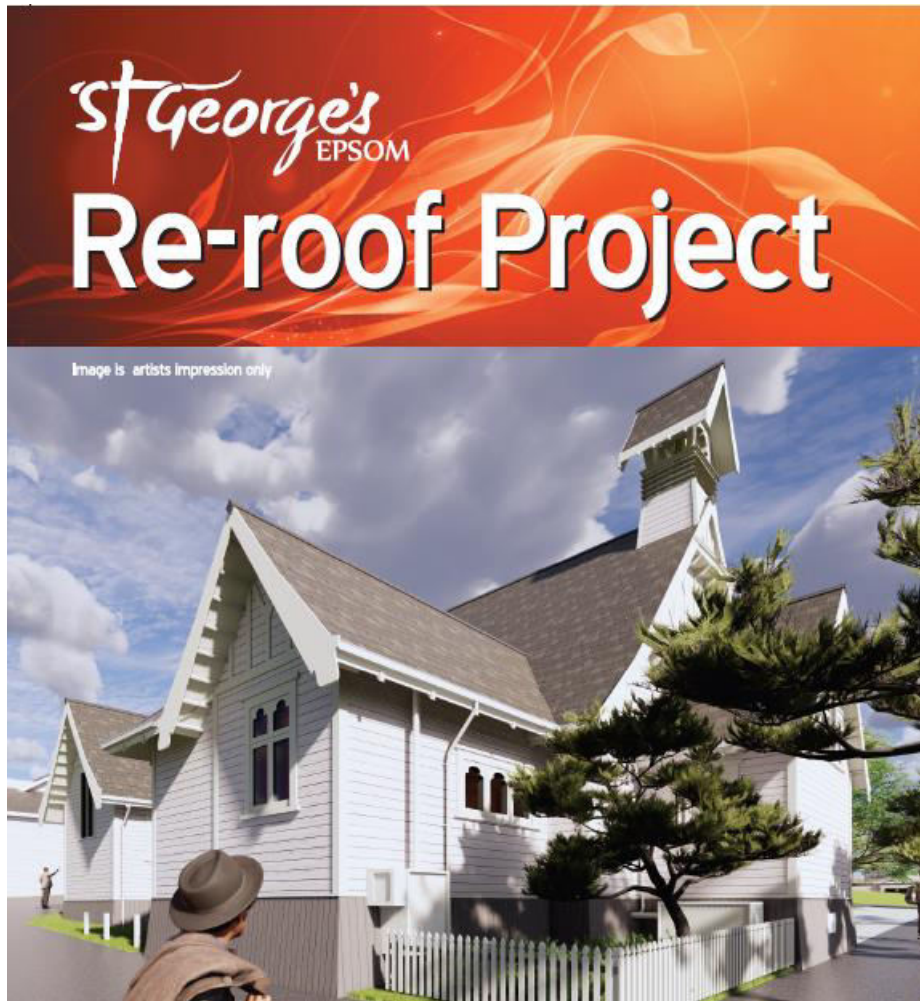

Now just over two weeks into the actual contract works, you might think that not much has happened. The scaffolding isn't even complete yet.

But when you think of the scaffolding work as effectively building a free-standing church structure out of scaffold pipe, including allowing eventual access to, and egress from the wooden church inside, including emergency exits, then you begin to appreciate the complexity of the scaffolding job. The scaffold structure must not touch the actual church building because of the risk of damaging the heritage structure.

Our explanatory sign has been placed on the front safety fence and a smaller sign explaining the route through the property to the hall and on to Halifax Avenue is also in place.

We're still hoping that another two weeks of fair weather will see the scaffolding complete, and plastic wrapped but there's some slack in the plan to allow for a little delay and the tile removal contractor will visit the site next week to check preparations and suss out any issues.

We are very grateful that donations to the roof fund have continued to come in, which will be invaluable to cover any contingencies.

**Steve Barnett**  
**Roof Project Lead**
