


Re-Roof Project: Weekly Update

Saturday 12 November

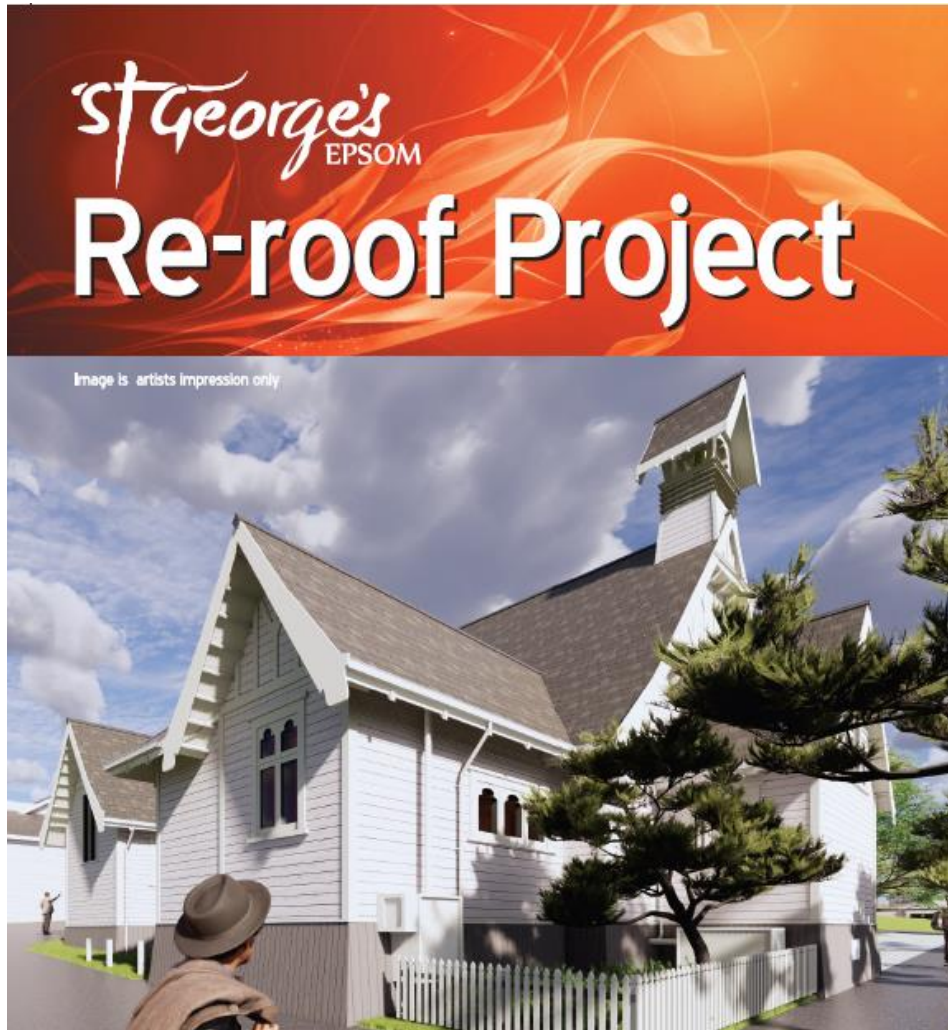

We are now seven weeks into the roof contract works, and progress has been a lot slower than we had expected.

Although the church is now plastic-wrapped except for the bell tower and front porch, wet weather has again slowed progress on the remaining scaffolding, which remains incomplete.

The asbestos tile removal contractor's start has been pushed back to around 24 November.

Steve Barnett, Project Lead
