


## Weekly Update 11

Saturday 17 December 2022

# St George's EPSOM Re-roof Project

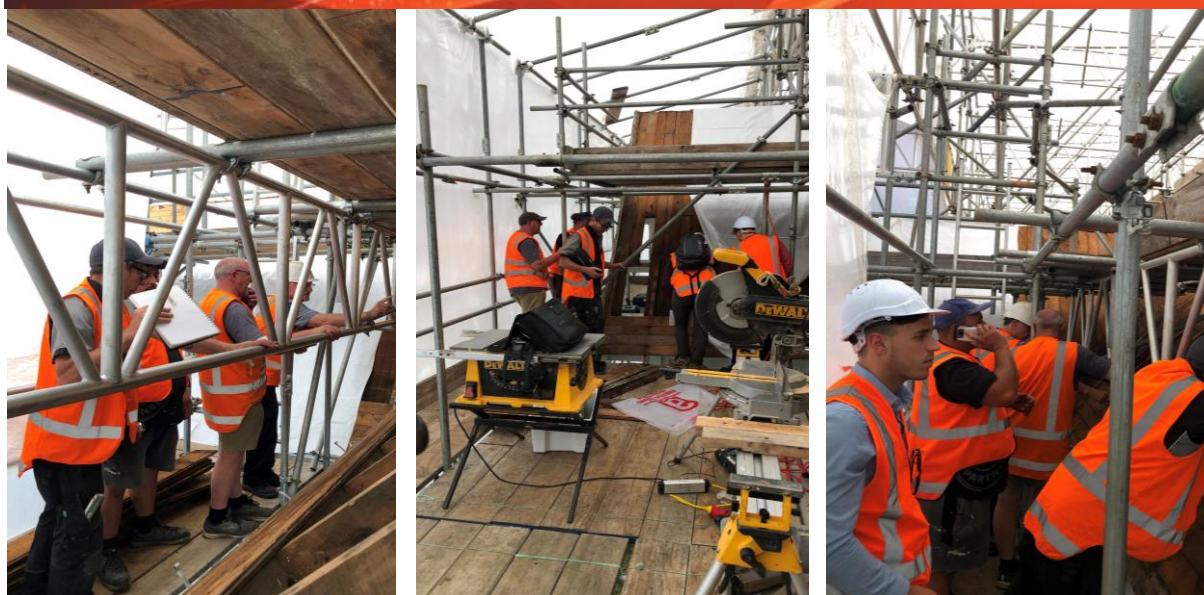

### Under the covers

Eleven weeks into the contract works, the good news is that despite having to reassess our method for structural strengthening, work has not been delayed. The half-dozen strong carpentry crew had a full programme repairing and replacing rotted timber in the eaves. This week they begin with strengthening work that doesn't need design approval. The rest of the work will proceed with approval during the course of the week.

As you can see above, there was no shortage of expertise to consult on the revised design. Architect, engineer, site foreman, site manager, construction boss, and I all collaborated to devise the plan, which must work for the thirteen different additions the original church roof structure has undergone. It is interesting to see how construction methods have evolved over the life of the building. At this stage we expect to recover some of the lost time and to stay within budget.

The carpentry crew will be back on the job straight after the statutory holidays.

**Steve Barnett, Project Lead**
