


Weekly Update 9

Saturday 3 December 2022

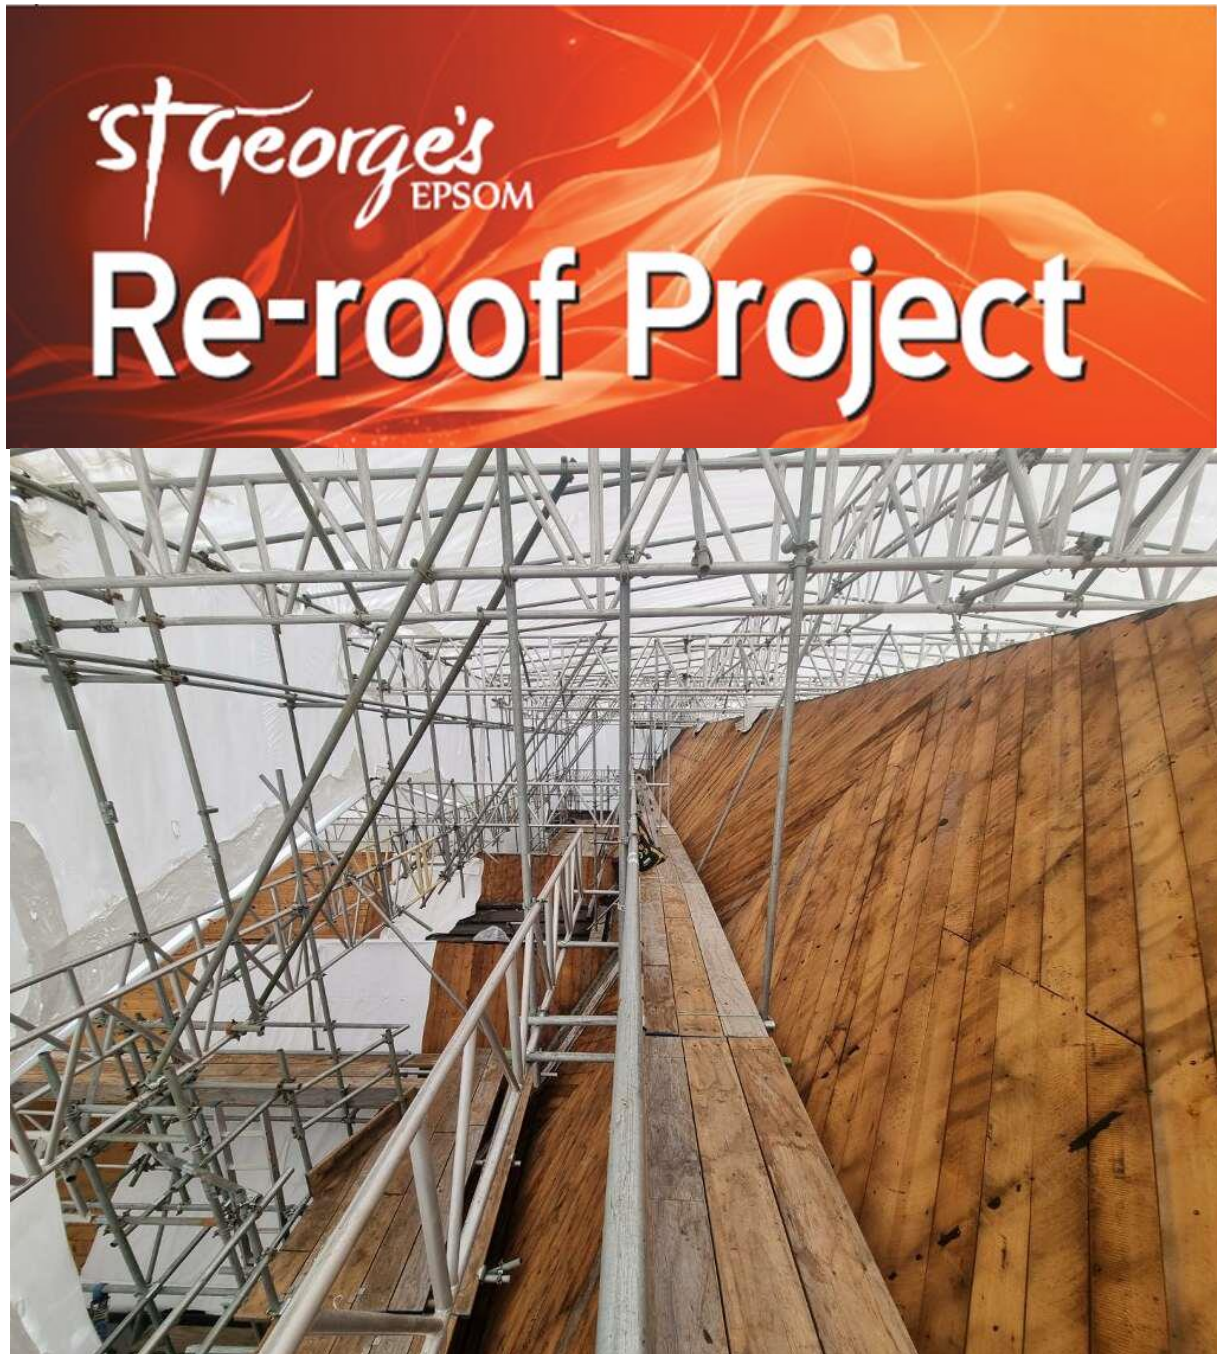

We are now nine weeks into the contract works and, except for the roadside porch, which is still uncovered, the church is a white elephant. Under the white skin, however, all of the asbestos cement roof tiles on the east side of the church have been removed, revealing a timber sub-structure different to that which was anticipated, based on the substructure evident at the eaves.

This may require redesign of the seismic strengthening and returning to the City Council to obtain consent to the required variation. We don't yet know what the cost implication will be, but we expect further delay to the start of carpentry works. Pray for a speedy resolution.

Steve Barnett, Project Lead
